ID	Task	Task Name	Duration	Start	Finish
1		მოსამზადებელი სამუშაოები	4 days	Thu 10/25/12	Tue 10/30/12
2		მიწის სამუშაოები	9 days	Wed 10/31/12	Mon 11/12/12
3		რკინა-ბეტონის საძირკვლის მოწყობა	14 days	Sun 11/11/12	Wed 11/28/12
4		რკინა-ბეტონის კარკასის მოწყობა (-1)	14 days	Mon 11/26/12	Thu 12/13/12
5		რკინა-ბეტონის კარკასის მოწყობა (0)	14 days	Sun 12/9/12	Wed 12/26/12
6		რკინა-ბეტონის კარკასის მოწყობა (1)	14 days	Mon 12/24/12	Thu 1/10/13
7		რკინა-ბეტონის კარკასის მოწყობა (2)	14 days	Tue 1/8/13	Fri 1/25/13
8		რკინა-ბეტონის კარკასის მოწყობა (3)	14 days	Thu 1/24/13	Tue 2/12/13
9		რკინა-ბეტონის კარკასის მოწყობა (4)	14 days	Wed 2/13/13	Mon 3/4/13
10		გარე მოპირკეთება	87 days	Fri 3/1/13	Sun 6/30/13
11		შიდა მოპირკეთება	66 days	Sat 6/1/13	Fri 8/30/13
12		გამწვანების მოწყობა	45 days	Mon 7/1/13	Fri 8/30/13
13		დასრულებითი სამუშაოები	22 days	Sun 9/1/13	Mon 9/30/13

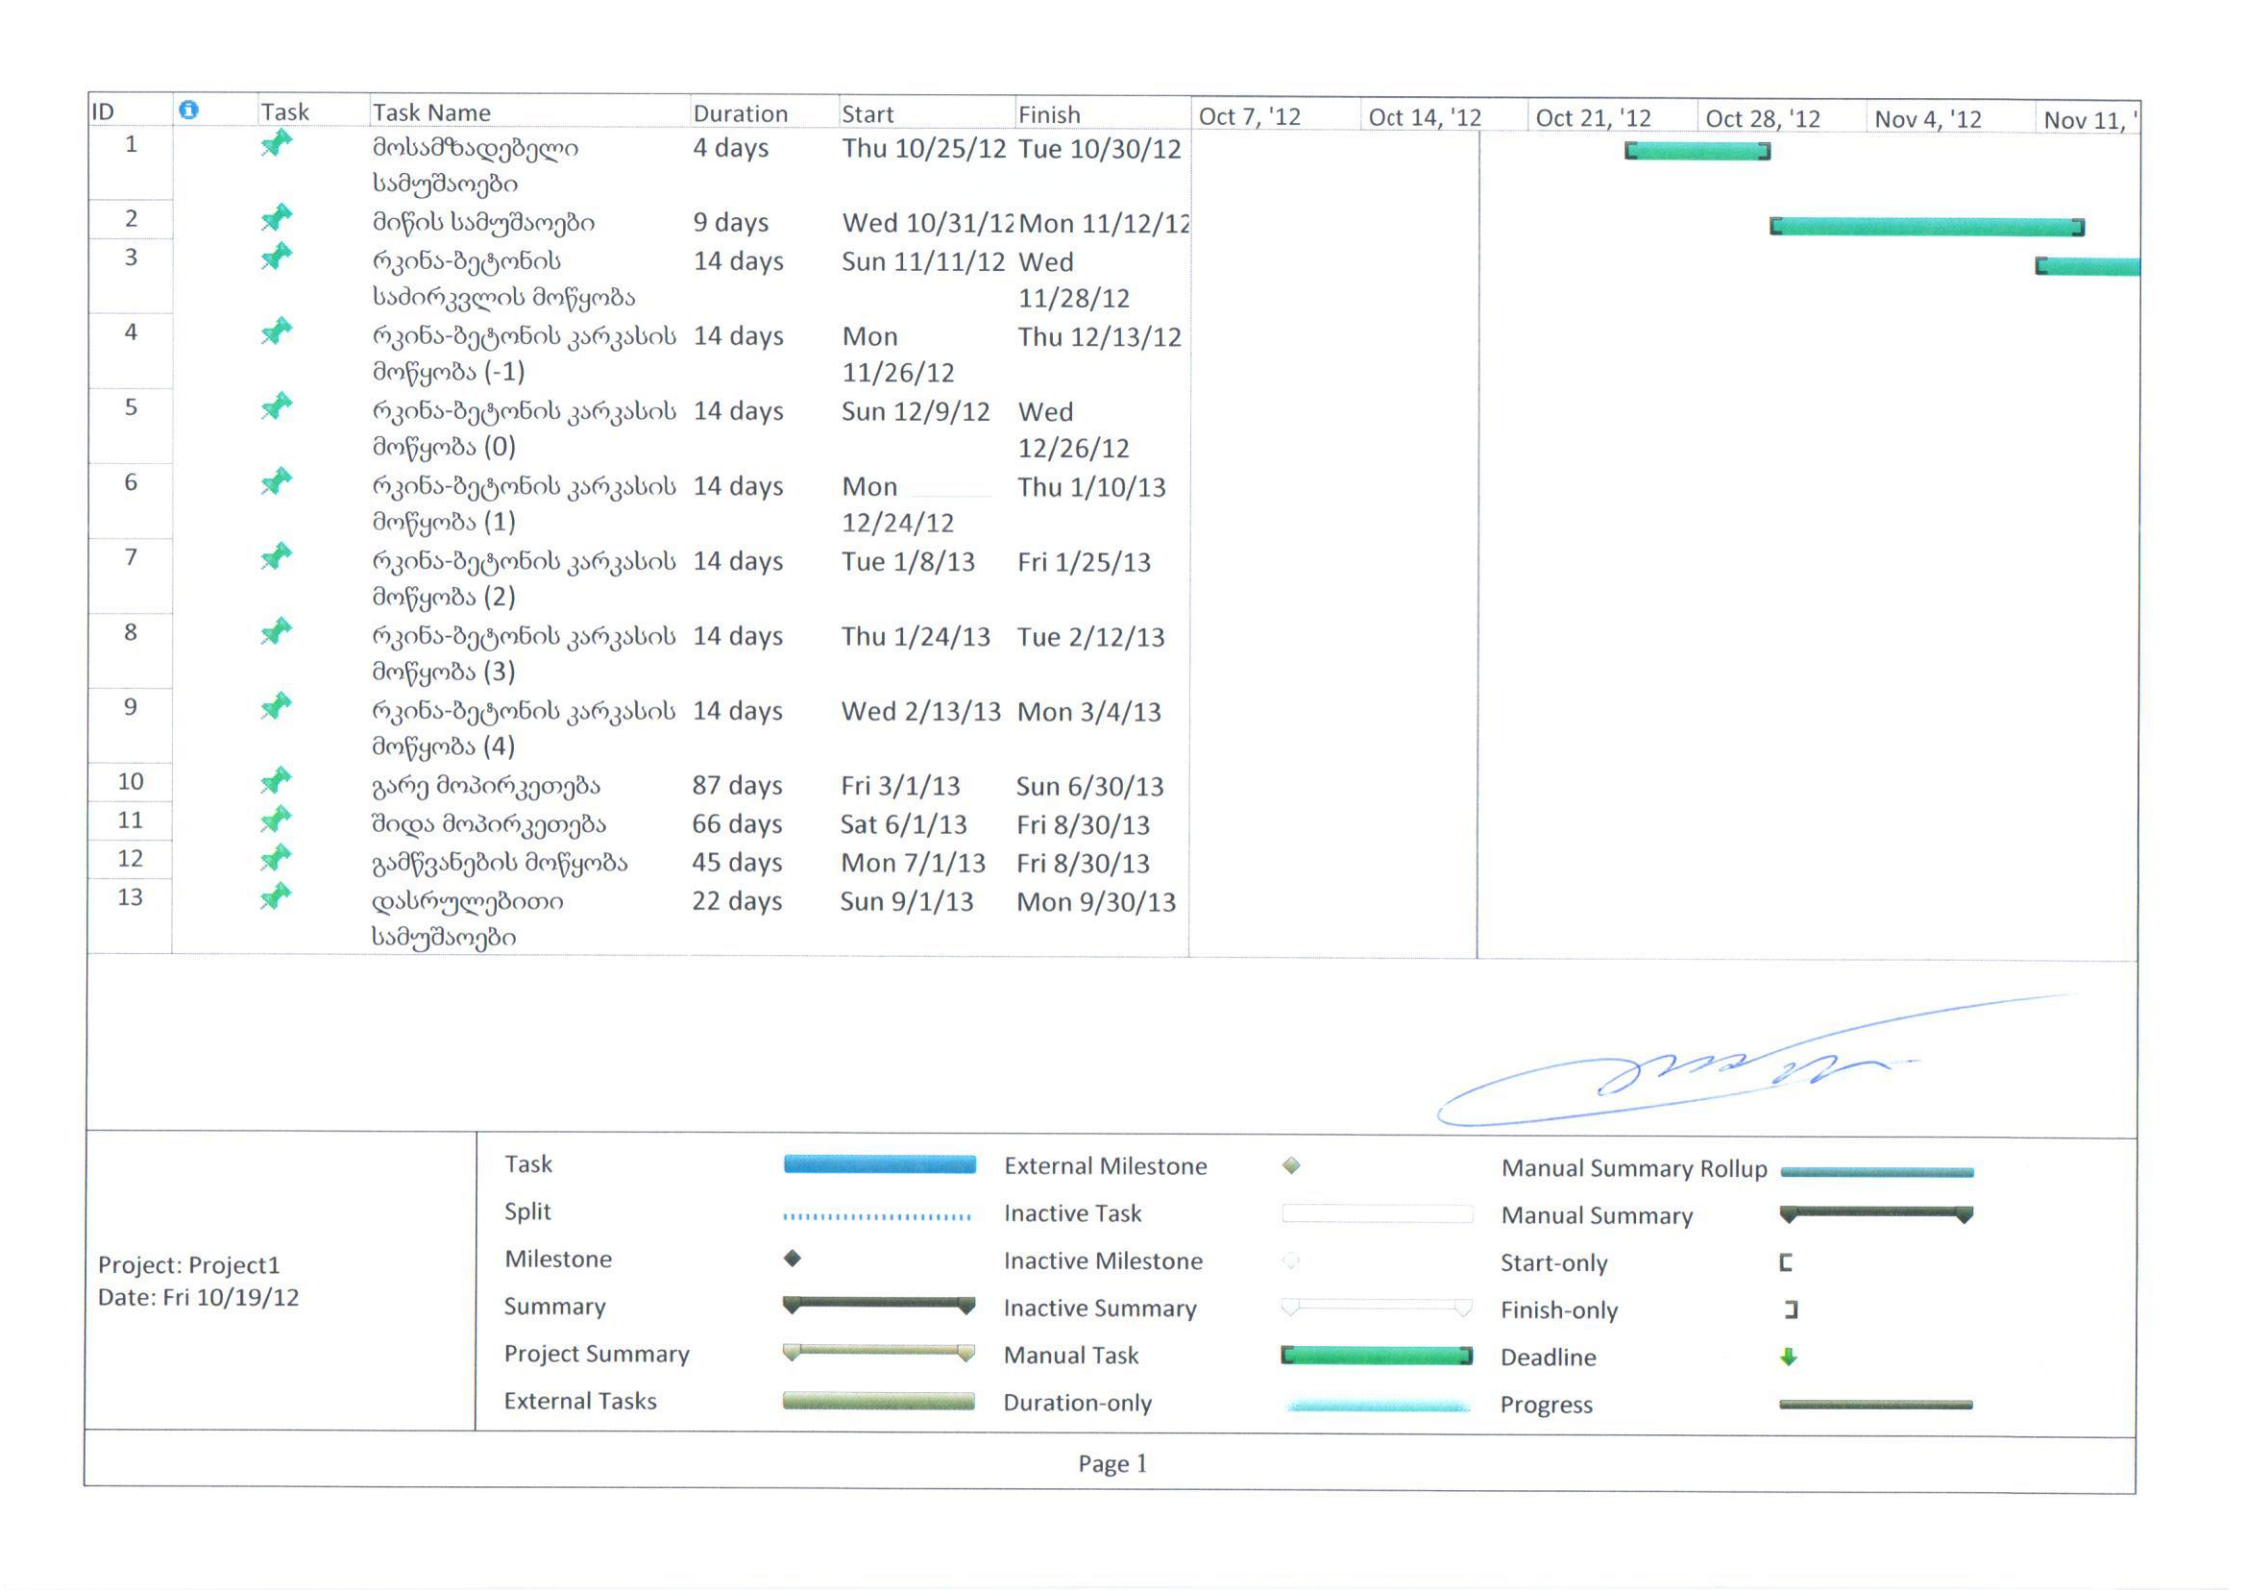

Project: Project1
Date: Fri 10/19/12

Task	External Milestone	Manual Summary Rollup	
Split	Inactive Task	Manual Summary	
Milestone	Inactive Milestone	Start-only	
Summary	Inactive Summary	Finish-only	
Project Summary	Manual Task	Deadline	
External Tasks	Duration-only	Progress	

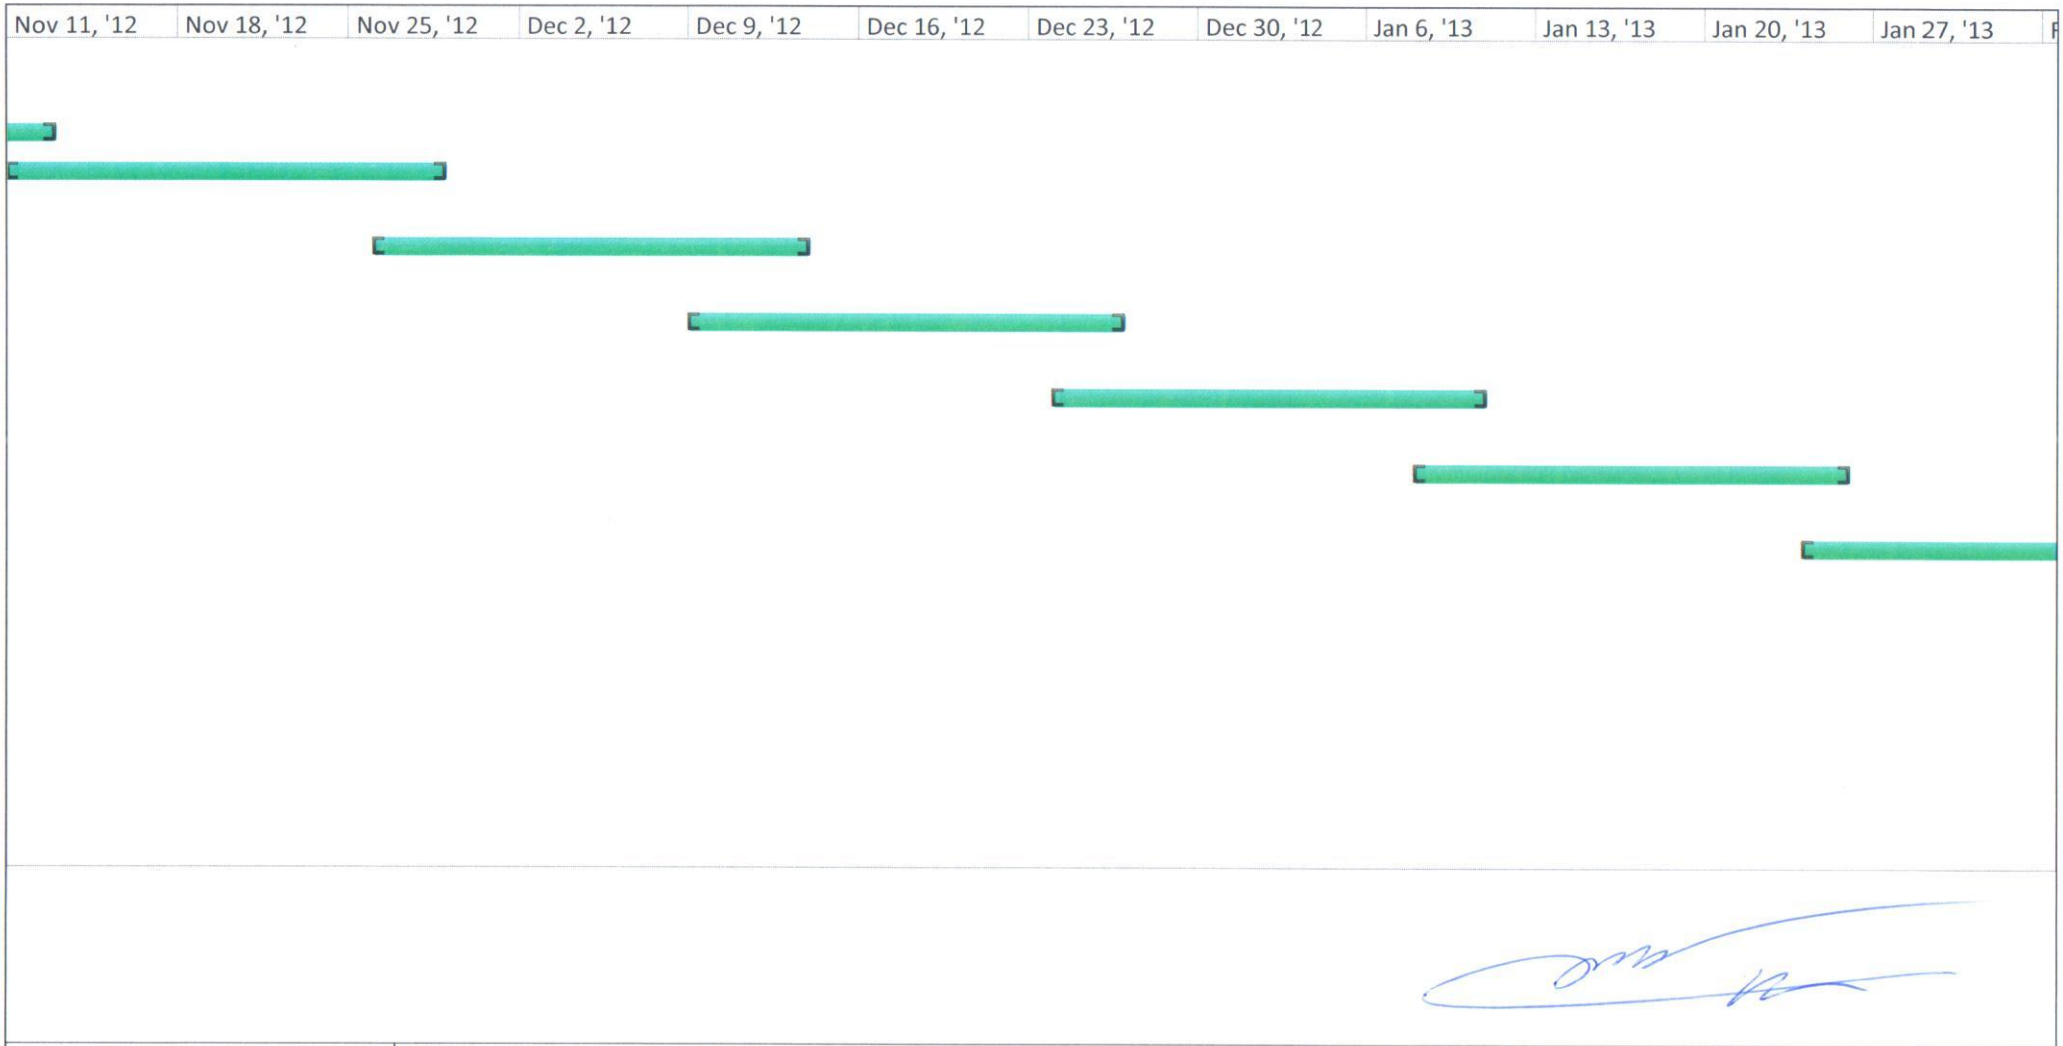

Project: Project1
Date: Fri 10/19/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	



Project: Project1
Date: Fri 10/19/12

Task	External Milestone		Manual Summary Rollup
Split	Inactive Task		Manual Summary
Milestone	Inactive Milestone		Start-only
Summary	Inactive Summary		Finish-only
Project Summary	Manual Task		Deadline
External Tasks	Duration-only		Progress



Project: Project1
Date: Fri 10/19/12

Task	External Milestone		Manual Summary Rollup
Split	Inactive Task		Manual Summary
Milestone	Inactive Milestone		Start-only
Summary	Inactive Summary		Finish-only
Project Summary	Manual Task		Deadline
External Tasks	Duration-only		Progress

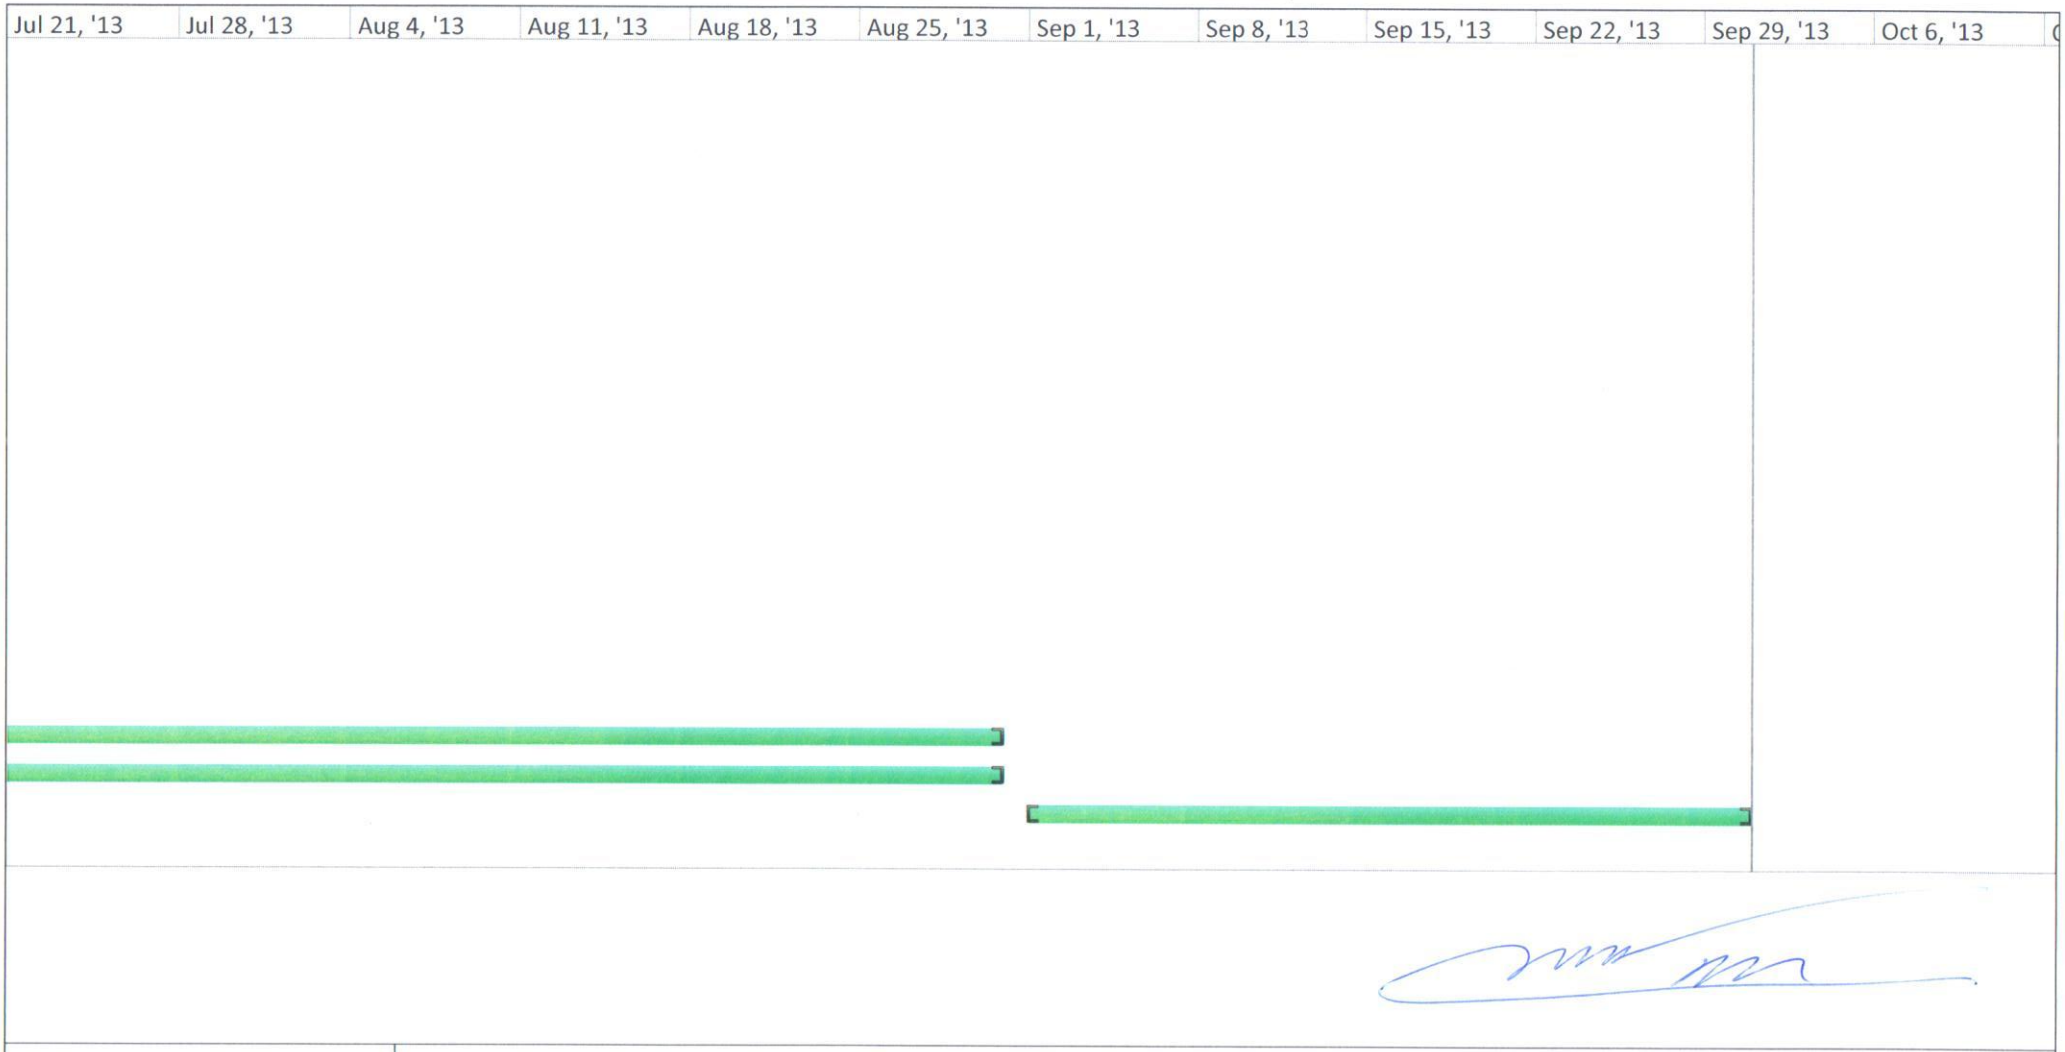

Project: Project1
Date: Fri 10/19/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	
